

CHANGE ORDER

Project: **Kittitas County Upper District Court Remodel** KC Project No.: **2012-004**
Owner: **Kitittas County** ART Project No. **1204**
Architect: **Architects Rasmussen Triebelhorn, AIA P/S** Change Order No.: **3**
Contractor: **M. Sevigny Construction, Inc.** Date: **10-Sep-2013**
(☐) No Change (☒) Addition (☐) Deduction

A "Change Order" is a written instrument prepared by the Architect and signed by the Owner, Contractor, and Architect, stating their agreement upon the following:
A change in work; the amount of the adjustment in contract sum, if any, and the extent of adjustment in the contract time, if any. A change order shall constitute final resolution of the matter addressed by the change order. Owner's signature reflects the Owner's agreement to the determination. Contractor may bill based upon any increase in the Contract Sum and, if Contractor disagrees with the cost or time adjustment, must follow the written notice requirements of Article 21 of the General Provisions of the Contract.

Plans and/or Specifications shall be changed as follows (refer to attachments for back-up information):

COP	Scope/Description of Change Work	Cost	Calendar Days
24	Courtroom chair rail extension	\$1,089.37	0
25	Sleeves or shafts at existing exhaust fans in attic insulation	\$312.46	0
26	Power and data revisions at Clerk Stations 102	\$3,775.71	0
27-R1	Tie court recording and public address systems together	\$2,746.72	5
28	Revise overhead door hieght	\$3,593.65	5
29	Delete acoustic tile from walls of courtroom	\$0.00	0
30	Loose floor tile removal & added floor prep (exclude COP 23)	\$384.56	0
31	Preventative maintenance to existing metal roof	\$2,115.08	0
32	Provide credit for underslab conduit not installed	\$0.00	0
33	Provide one additional 24-port patch panel on IT rack	\$403.47	0
34	Electrical inspector directed corrections/ revisions	\$584.05	0

Subtotals	\$15,005.07	10
WSST @ 8.0%	\$1,200.41	
Totals This Change Order	\$16,205.48	10

Attachments: PRs/COPs # 24 - 26, 27-R1, and 28 - 34.

The Original Contract Sum, including WSST, was	\$432,000.00
Total of Change Orders prior to this Change Order was	\$37,378.50
The Contract Sum prior to this Change Order was	\$469,378.50
The Contract Sum will be increased by this change order in the amount of	\$16,205.48
The new Contract Sum after this Change Order will be	\$485,583.98

The date for Substantial Completion for the overall project shall be changed by zero (10) calendar days.
The new date for Substantial Completion shall be July 16, 2013.

APPROVALS:

Signature
Obie O'Brien, Kittitas County Commissioner

Date



9/10/2013

Signature
David Head; Architect

Date

Signature
M. Sevigny Construction, Inc. (Representative)

Date

M SEVIGNY CONSTRUCTION INC.**1212 N 16th AVENUE #1****YAKIMA, WA. 98908****Upper District Court Remodel****KITTITAS COUNTY****PROJECT # PW12-022****DATE: 5/16/13****PROPOSAL: PR # 24****Chair Rail**

#	ITEM DETAIL		SUB CONTRACTOR	GENERAL CONTRACTOR		TOTAL
1	Cabinet Tech		912.00			912.00
2	Cleanup			50.00		50.00
3		-			-	-
4		-			-	-
5					-	-
6					-	-
7					-	-
8					-	-
9					-	-
10					-	-
11					-	-
12					-	-
	SUBTOTAL	-	912.00	50.00	-	962.00
		-			-	-
	SUBTOTAL	-	912.00	50.00	-	962.00
	SUBCONTRACTOR 8%		72.96			72.96
	GENERAL 15%	-		7.50	-	7.50
	SUBTOTAL	-	984.96	57.50	-	1,042.46
	BOND AND INSURANCE 2.5%	-	24.62	1.44	-	26.06
	SAFETY 2%	-	19.70	1.15	-	20.85
	TOTAL PROPOSAL	-	1,029.28	60.09	-	1,089.37
	TIME REQUIRED TBD DAYS					
	M SEVIGNY CONSTRUCTION INC.					
	MATTHEW SEVIGNY					



Cabinets & Millwork

CABINTL001JL

PO Box 2872 • Yakima, WA 98907

www.cabinettech.com

(509) 575-0180 Tel

(509) 453-0014 Fax

866-862-8324 Toll Free

Change Request

To: M SEVIGNY CONSTRUCTION INC
1212 N 16TH AVE #1
YAKIMA, WA 98902
Ph: 9454468/9493547 Fax: 509-424-3222

Number: 2

Date: 3/27/13

Job: 13-30-010 SEVIGNY CONST- KITTITAS COURT

Phone:

Description: PR #5 ADDED CHAIR RAIL

We are pleased to offer the following specifications and pricing to make the following changes:

IN COURTROOM 111, EXTEND THE LENGTH OF THE CHAIR RAILS TO THE NORTH WALL AND THEN TO THE ADJACENT FRAME OF DOORS 104B AND 105B.

The total amount to provide this work is

\$912.00

If you have any questions, please contact me at 509-453-6581.

Submitted by: CABINET TECH, LLC

Approved by: _____

Date: _____

Cc:



ARCHITECTS
RASMUSSEN
TRIEBELHORN AIA/PS

Number 9 Saint Helens, Ste. D
The Henry Drum House
Tacoma WA 98402

Phone: 253 572-5511
Fax: 253 572-5515
www.a-r-t.org

Peter T.S. Rasmussen, FAIA, Principal
Kenn D. Triebelhorn, AIA, Principal
Rhonda A. Gillogly, AIA, Principal

PROPOSAL REQUEST

- ☒ Owner
☒ Architect
☒ Contractor
☐ Field
☐

AIA DOCUMENT G709

PROJECT:
Kittitas County
Upper District Court Remodel
700 East 1st Street
Cle Elum, WA 98922

PROPOSAL REQUEST NO: **24**

REFERENCE NO.

OWNER:
Kittitas County
205 West 5th Avenue
Ellensburg, WA 98926

ISSUE DATE: **May 9, 2013**

OWNER'S PROJECT NO. **2012-004**

TO:
M. Seigny Construction, Inc.
1251 Lucy Lane
Zillah, WA 98953

ART'S PROJECT NO. **1204**

CONTRACT DATED: **January 8, 2013**

Please submit an itemized quotation for changes in the Contract Sum and/or Time incidental to proposed modifications to the Contract Documents described herein.

THIS IS NOT A CHANGE ORDER NOR A DIRECTION TO PROCEED WITH THE WORK DESCRIBED HEREIN.

Description: (Written description of the Work)

As previously described in email on 3/8/2013:

In Courtroom 111, extend the length of the chair rails to the north wall and then to the adjacent frame of doors 104B and 105B. (Use same figures that were submitted by M. Seigny as an addition to COP 5).

Attachments: (List attached documents that support description)

None

ARCHITECTS RASMUSSEN TRIEBELHORN

By: David L. Head

M SEVIGNY CONSTRUCTION INC.**1212 N 16th AVENUE #1****YAKIMA, WA. 98908****Upper District Court Remodel****KITTITAS COUNTY****PROJECT # PW12-022****DATE: 5/16/13****PROPOSAL: PR # 25****Fan Sleeves**

#	ITEM DETAIL		SUB CONTRACTOR	GENERAL CONTRACTOR		TOTAL
1	Materials			100.00		100.00
2	Labor			110.00		110.00
3	Cleanup	-		50.00	-	50.00
4		-				-
5					-	-
6					-	-
7					-	-
8						-
9						-
10						-
11						-
12						-
	SUBTOTAL	-	-	260.00	-	260.00
		-			-	-
	SUBTOTAL	-	-	260.00	-	260.00
	SUBCONTRACTOR 8%		-			-
	GENERAL 15%	-		39.00	-	39.00
	SUBTOTAL	-	-	299.00	-	299.00
	BOND AND INSURANCE 2.5%	-	-	7.48	-	7.48
	SAFETY 2%	-	-	5.98	-	5.98
	TOTAL PROPOSAL	-	-	312.46	-	312.46
	TIME REQUIRED TBD DAYS					
	M SEVIGNY CONSTRUCTION INC.					
	MATTHEW SEVIGNY					

APPROVED FOR CHANGE ORDER #3
David Head, ART 6/12/2013



ARCHITECTS
RASMUSSEN
TRIEBELHORN AIA/AS

Number 9 Saint Helens, Ste. D
The Henry Drum House
Tacoma WA 98402

Phone: 253 572-5511
Fax: 253 572-5515
www.a-r-t.org

Peter T.S. Rasmussen, FAIA, Principal
Kenn D. Triebelhorn, AIA, Principal
Rhonda A. Gilling, AIA, Principal

PROPOSAL REQUEST

- ☒ Owner
☒ Architect
☒ Contractor
☐ Field
☐

AIA DOCUMENT G709

PROJECT:
Kittitas County
Upper District Court Remodel
700 East 1st Street
Cle Elum, WA 98922

PROPOSAL REQUEST NO: **25**

REFERENCE NO.

OWNER:
Kittitas County
205 West 5th Avenue
Ellensburg, WA 98926

ISSUE DATE: **May 8, 2013**

TO:
M. Seigny Construction, Inc.
1251 Lucy Lane
Zillah, WA 98953

OWNER'S PROJECT NO. **2012-004**

ART'S PROJECT NO. **1204**

CONTRACT DATED: **January 8, 2013**

Please submit an itemized quotation for changes in the Contract Sum and/or Time incidental to proposed modifications to the Contract Documents described herein.

THIS IS NOT A CHANGE ORDER NOR A DIRECTION TO PROCEED WITH THE WORK DESCRIBED HEREIN.

Description: (Written description of the Work)

Provide sleeves or shafts around each existing exhaust fan located in the attic to prevent the migration of blown-in insulation over them. These sleeves or shafts shall be made of sheet metal, rigid cardboard, or sono-tube type material. They shall extend from the bottom of the trusses to a minimum of 4 inches above the top insulation. No insulation shall remain within the sleeves or shafts. The sleeves' or shafts' footprint shall be reasonably small as to not create large areas of displaced insulation.

Attachments: (List attached documents that support description)

None

ARCHITECTS RASMUSSEN TRIEBELHORN

By: David L. Head

M SEVIGNY CONSTRUCTION INC.

1212 N 16th AVENUE #1

YAKIMA, WA. 98902

Upper District Court Remodel

KITTITAS COUNTY

PROJECT # PW12-022

DATE: 5/28/13

PROPOSAL: COP 26

Clerks 102 Changes

#	ITEM DETAIL	SUB CONTRACTOR	GENERAL CONTRACTOR	TOTAL
1	Item 1	925 -1,850.00		1,850.00
2	Item 2	(1,775.00)		(1,775.00)
3	Item 3	- 270.00	-	270.00
4	Item 4	- 990.00		990.00
5	Item 5	545.00	-	545.00
6	Item 6	1,309.62	-	1,309.62
7	Item 7	920.56	-	920.56
8	Item 4 Open wall cut patch		150.00	150.00
9				-
10				-
11				-
12				-
	SUBTOTAL	- 3185.18 -4,110.18	150.00	- 4,260.18
	SUBTOTAL	- 3185.18 -4,110.18	150.00	- 4,260.18
	SUBCONTRACTOR 8%	254.81 328.81		328.81
	GENERAL 15%	-	22.50	22.50
	SUBTOTAL	- 3440.62 -4,438.99	172.50	- 4,611.49
	BOND AND INSURANCE 2.5%	- 86.02 110.97	4.31	- 115.29
	SAFETY 2%	- 68.81 88.78	3.45	- 92.23
	TOTAL PROPOSAL	- 3595.45 -4,638.75	180.26	- 4,819.01
				3775.71
	TIME REQUIRED TBD DAYS			
	M SEVIGNY CONSTRUCTION INC.			
	MATTHEW SEVIGNY			

APPROVED FOR CHANGE ORDER #3
David Head, ART 6/12/2013



5-24-13

M. Seigny Construction
1212 N 16th Ave #1
Yakima, WA 98902

Attn. Matt Seigny

Re: Kittitas Co. Upper Court.
COP #6 Revised #2

The following is the cost breakdown for PR26. This price is based on all cables attached to the underside of the existing ceiling. Walls to be opened and repaired by others for item #4. Item #1 is priced using original purchased poles.

1)				
	10 cables	1000ftX.2	200.00	
	Labor data	5X65	325.00	
	Subcontract data	10x40	400.00	
	Material		200.00	
	Labor		325.00	
	Subcontract		400.00	
	Total cost		925.00	+ 1850 + 925
2)				
	8 cables	800x.2	-160.00	
	Return wiremold		-660.00	
	Delete circuit	100X.5	-50.00	
	Labor wiremold	4X65	-260.00	
	Labor circuit	1x65	-65.00	
	Labor data	4x65	-260.00	
	Subcontract data	8x40	-320.00	
	Material		-870.00	
	Labor		-585.00	
	Subcontract		-320.00	
	Total credit		-1775.00	- 1775
3)				
	New circuit	50x.5	25.00	
	Box and outlet	2x25	50.00	
	Labor circuit	1x65	65.00	
	Labor box and outlets	2x65.00	130.00	+ 270

Material		75.00
Labor		195.00
Total cost		270.00
4)		
Cable	1000x.2	200.00
Labor cable/walls	6x65	390.00
Subcontract data	10x40	400.00
Material		200.00
Labor		390.00
Subcontract		400.00
Total cost		990.00
5)		
Cable	400x.2	80.00
Wiremold and box		70.00
Labor data	1.5x65	97.50
Labor wiremold	1.5x65	97.50
Subcontract	2x100	200.00
Material		150.00
Labor		195.00
Subcontract		200.00
Total cost		545.00
6)		
Labor	3.5x65	227.50
Equipment	pick up	100.00
Subcontract	new data rack	909.37
P&O		72.75
Total cost		1309.62
7)		
Temp phone cable phase 1, ground		200.00
Labor admin	1x65	65.00
Subcontract	12 pair cable to demark, 3 cat 5 cables temp clerk	607.00
P&O		48.56
Total cost		920.56

+ 990

+ 545

+ 1309.62

+ 920.56

Sincerely,

Tim Prater



ARCHITECTS
RASMUSSEN
TRIEBELHORN AIA/PS

Number 9 Saint Helens, Ste. D
The Henry Drum House
Tacoma WA 98402

Phone 253 572-5511
Fax 253 572-5515
www.a-rt.org

Peter T.S. Rasmussen, FAIA, Principal
Kenn D. Triebelhorn, AIA, Principal
Rhonda A. Gillogly, AIA, Principal

PROPOSAL REQUEST

- ☒ Owner
☒ Architect
☒ Contractor
☐ Field
☐

AIA DOCUMENT G709

PROJECT:
**Kittitas County
Upper District Court Remodel
700 East 1st Street
Cle Elum, WA 98922**

PROPOSAL REQUEST NO: **26**

REFERENCE NO.

OWNER:
**Kittitas County
205 West 5th Avenue
Ellensburg, WA 98926**

ISSUE DATE: **May 10, 2013**

TO:
**M. Seigny Construction, Inc.
1251 Lucy Lane
Zillah, WA 98953**

OWNER'S PROJECT NO. **2012-004**

ART'S PROJECT NO. **1204**

CONTRACT DATED: **January 8, 2013**

Please submit an itemized quotation for changes in the Contract Sum and/or Time incidental to proposed modifications to the Contract Documents described herein.

THIS IS NOT A CHANGE ORDER NOR A DIRECTION TO PROCEED WITH THE WORK DESCRIBED HEREIN.

Description: (Written description of the Work)

Revise the power, telephone and data within Clerk Stations 102 as shown in the attached power/signal floor plan, and as outlined below.

1. Provide (4) Wiremold 25DTP/AMTC series power poles in lieu of (4) discontinued NP600 wiremold power poles, in revised locations shown on attached plan. Exact locations to be coordinated by Owner/Architect in field prior to final placement. (2) power poles shall have (4) duplex receptacles and (2) data outlets with (3) Cat 5e cables to each. (2) power poles shall have (4) duplex receptacles and (1) data outlets with (3) Cat 5e cables to each.
2. Delete and provide credit for all 2-channel wiremold from west wall, including (2) 4-plex receptacles, (2) data outlets and associated conduit and wire.
3. Relocate (1) existing duplex receptacle impacted by the installation of the door and relite to Court Admin 103 southward to wall in common with Break 108. Provide 1/2"C-#12 CU Conductors and reconnect to existing circuit.
4. Contractor shall provide (2) Cat 5e cables to all existing data locations in Clerk Station 102.
5. Add (2) analog phone receptacles at locations shown. Wiring shall be routed to phone demarcation location. Provide surface wiremold from above ceiling to new surface mounted analog phone outlet for wiring.
6. Provide a new Chatsworth 46353-503 rack with wire management per ESK-7 and new 24-port patch panel to match existing to accommodate new data cabling.

Attachments: (List attached documents that support description)

Sketch ESK-6 (Revised power/signal floor plan for Clerk Stations 102)
Sketch ESK-7 (Data Rack detail)

ARCHITECTS RASMUSSEN TRIEBELHORN



By: David L. Head

ELECTRICAL NOTES:

- 9 POWER POLE LOCATION ARE DEPENDANT ON FURNITURE LOCATIONS. CONTRACTOR SHALL VERIFY LOCATION OF POWER POLES WITH OWNER PRIOR TO FINAL INSTALLATION.
- 10 CONTRACTOR SHALL PROVIDE AN ANALOG PHONE LINE AT THIS LOCATION FOR FAX OR POSTAGE METER.
- 11 CONTRACTOR SHALL PROVIDE 1/2"C-#12 CU CONDUCTORS AND RELOCATE EXISTING RECEPTACLE TO WITH-IN 1 FOOT OF NEW DOOR JAM.

WIREMOLD 25DTP/AMTC SERIES
2-CHANNEL POWER POLE OR
EQUAL WITH (2) DATA OUTLETS
WITH (3) CAT 5e CABLES EACH
AND (4) DUPLEX RECEPTACLES.

WIREMOLD 25DTP/AMTC SERIES
2-CHANNEL POWER POLE OR
EQUAL WITH (1) DATA OUTLET
WITH (3) CAT 5e CABLES AND
(4) DUPLEX RECEPTACLES.

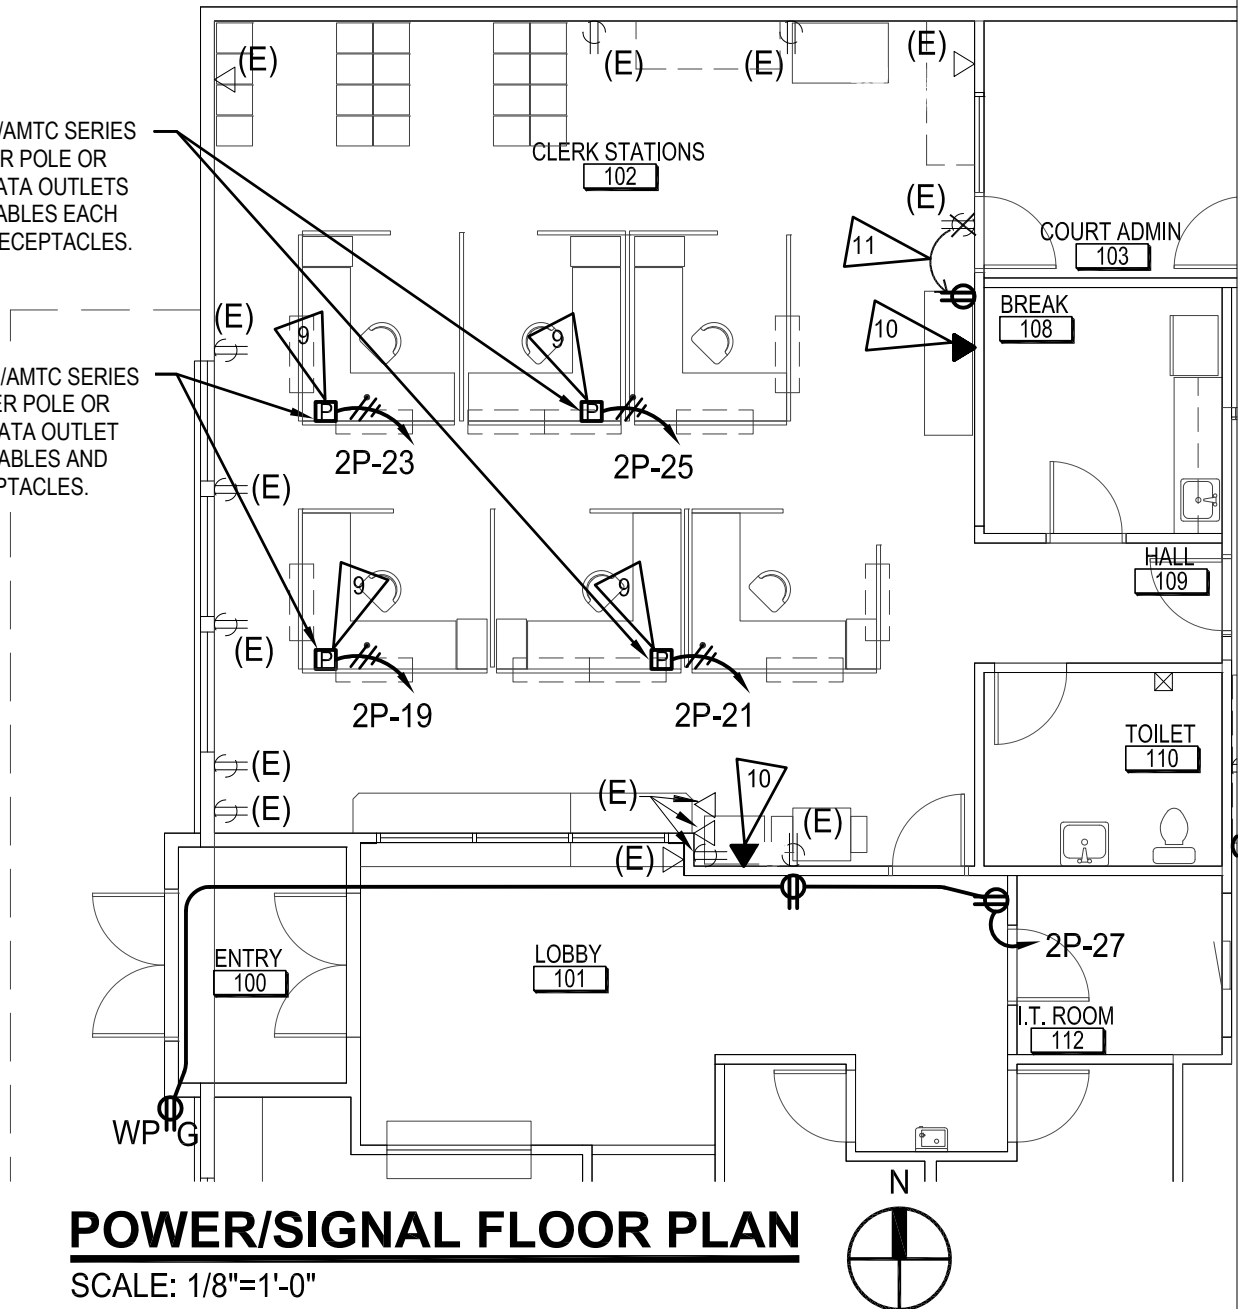

CROSS ENGINEERS, INC

6509 6th Avenue
Tacoma, WA 98406
info@crossengineers.com

Phone: (253) 759-0118
Job Number: 12-072

PROJECT TITLE : KITTITAS COUNTY COURTS


PROJECT # : 12-072

DATE : MAY 10, 2013

ESK-6


GENERAL EQUIPMENT IDENTIFICATION:

- 01 RACK, CHATSWORTH - 46353-503
- 02 HORIZONTAL CABLE MANAGEMENT, CHATSWORTH - 30131-719
- 03 VERTICAL CABLE MANAGEMENT, CHATSWORTH - 11729-503
- 04 DATA EQUIPMENT

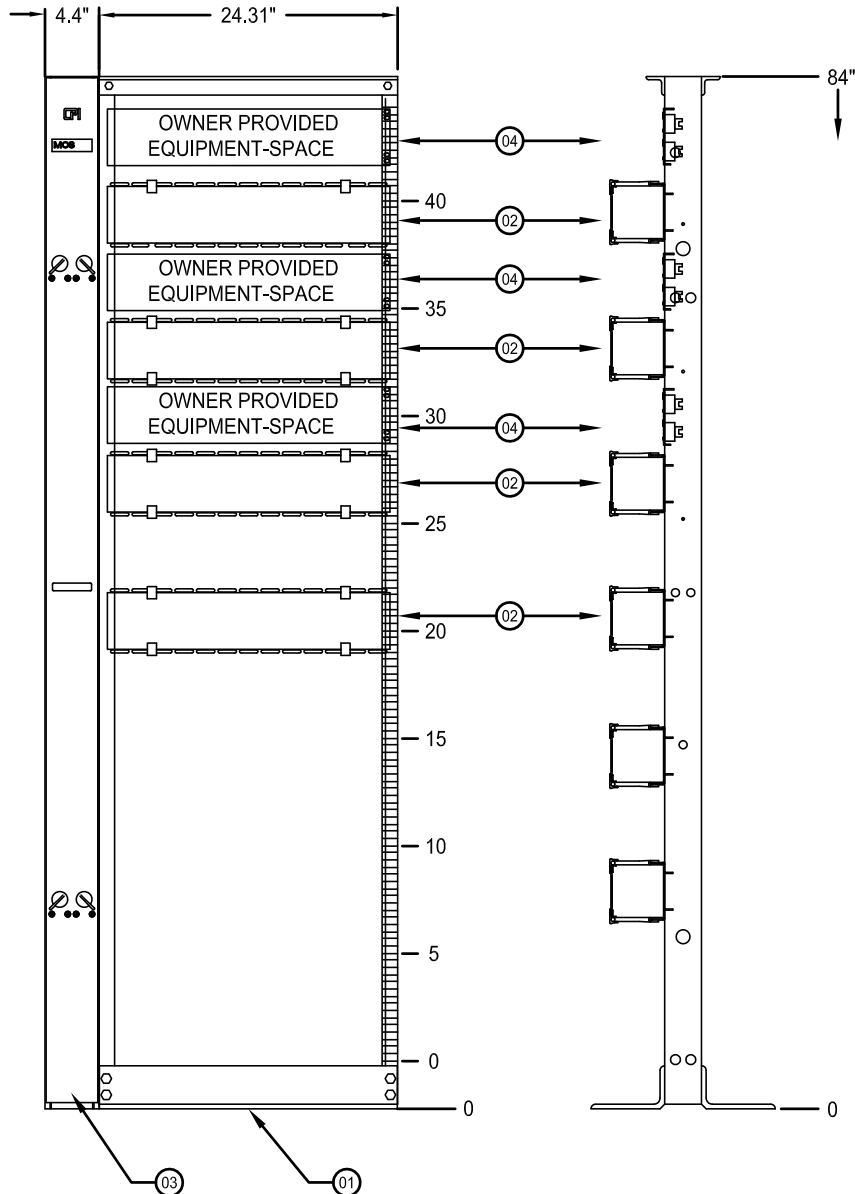

RACK MOUNTING ELEVATION

NOT TO SCALE



CROSS ENGINEERS, INC

6509 6th Avenue
Tacoma, WA 98406
info@crossengineers.com

Phone: (253) 759-0118
Job Number: 12-072

PROJECT TITLE : KITTITAS COUNTY COURTS

PROJECT # : 12-072

DATE : MAY 10, 2013

ESK-7

YAKIMA, WA. 98902

Existing Court Equipment

(D.L.H. 9/10/2013)

APPROVED FOR CHANGE ORDER #3
David Head, ART 6/27/2013



6-17-13

M. Seigny Construction
1212 N 16th Ave #1
Yakima, WA 98902

Attn. Matt Seigny

Re: Kittitas Co. Upper Court.
COP #7 PR 27

The following is the cost breakdown for PR27 to install cabling for the sound system as requested by the owner.

Subcontract material	\$573.00
Subcontract Labor	\$1152.00
P&O	\$138.00
Prater Equipment	\$150.00
Prater Labor	\$300.00
P&O	\$ 67.50
 Total cost	 \$ 2380.50

Sincerely,

Tim Prater



ARCHITECTS
RASMUSSEN
TRIEBELHORN AIA/PS

Number 9 Saint Helens, Ste. D
The Henry Drum House
Tacoma WA 98402

Phone 253 572-5511
Fax 253 572-5515
www.a-rt.org

Peter T.S. Rasmussen, FAIA, Principal
Kenn D. Triebelhorn, AIA, Principal
Rhonda A. Gillogly, AIA, Principal

PROPOSAL REQUEST

- ☒ Owner
☒ Architect
☒ Contractor

AIA DOCUMENT G709

PROJECT:

**Kittitas County
Upper District Court Remodel
700 East 1st Street
Cle Elum, WA 98922**

PROPOSAL REQUEST NO: **27-R1**

REFERENCE NO.

OWNER:

**Kittitas County
205 West 5th Avenue
Ellensburg, WA 98926**

ISSUE DATE: **May 28, 2013**
Revised June 27, 2013

OWNER'S PROJECT NO. **2012-004**

TO:

**M. Seigny Construction, Inc.
1251 Lucy Lane
Zillah, WA 98953**

ART'S PROJECT NO. **1204**

CONTRACT DATED: **January 8, 2013**

Please submit an itemized quotation for changes in the Contract Sum and/or Time incidental to proposed modifications to the Contract Documents described herein.

THIS IS NOT A CHANGE ORDER NOR A DIRECTION TO PROCEED WITH THE WORK DESCRIBED HEREIN.

Description: (Written description of the Work)

1. Within Courtroom 111, install the Owner's existing court recording and assisted listening systems in proper functioning order. Components included are outlined below. Modify cable ends (or run new wire) as required when routing through conduit, or at floor box jacks. Excess cable lengths shall be maintained and coiled, unless otherwise noted. Cables not in conduit shall be routed neatly and bundled where appropriate. Cables at the judge's bench shall be routed below and secured to the counters.
 - a. Computer with recording software - locate adjacent to west casework of clerk's desk, and extend cables to mixer/infrared modulator. Fed from matrix out to Toa mixer in I.T. room.
 - b. Mixer - locate adjacent to west casework of clerk's desk.
 - c. Infrared modulator - locate adjacent to west casework of clerk's desk.
 - d. Assisted listening transmitter - mounted on north wall adjacent, and extend cable through previously installed 1" conduit to equipment at clerk's desk. Connect power cord to above ceiling receptacle, added by PR 01, and coil excess cord at desk.
 - e. Judge's microphone - at judges bench, extend cable to Toa mixer in I.T. room.
 - f. Witness' microphone - at witness stand, extend cable to Toa mixer in I.T. room.
 - g. Prosecutor's microphone - on west table, cable to jack in west floor box.
 - h. Defendant's microphone - on east table, cable to jack in east floor box.
 - i. West floor box - install microphone jack, attach and extend cable through previously installed spare 1" conduit to Toa mixer in I.T. room.
 - j. East floor box - install microphone jack, attach and extend cable through previously installed spare 1" conduit to Toa mixer in I.T. room. Share conduit with cable of west floor box.
2. Provide and install one data receptacle in the east electrical/data floor box within Courtroom 111. Connect with Cat 5e cable through previously installed spare 1" conduit back to the data rack in I.T. 112. Between floor boxes this cable shall be routed with that noted in item 1j above.
3. Modify court recording system to be tied to the public address system, and for the public address microphones to be tied to the court recording system. Provide switching to allow court microphones to be shut off from public address speakers. Add a receiver to these tied systems. Relocate PA controls to the clerk's desk.
4. Replace two of the four PA wireless microphones with two body-pack microphone units.
5. Tie all microphones to hearing assistance modulator through Toa mixer matrix. Provide capability for one body-pack mic to support headset and fed via hearing assistance modulator channel B as translator system.

Attachments: (List attached documents that support description) None

ARCHITECTS RASMUSSEN TRIEBELHORN

By: David L. Head

Upper District Court Remodel
KITTITAS COUNTY
PROJECT # PW12-022
DATE: 6/22/13
PROPOSAL: COP 28
Rework Overhead Door

APPROVED FOR CHANGE ORDER #3
David Head, ART 7/3/2013



1118A N. 6th AVE.
YAKIMA, WA 98902
Contractor License #SCIDO**022MO

Page 1 of 2

Phone: (509) 575-7955

Fax: (509) 575-6964

E-mail: chris@scidoors.com

www.scidoors.com

PROPOSAL/CONTRACT

DATE: 6-21-13

TO: M. SEVIGNY CONSTRUCTION, INC.

ATTN: MATT

SUBJECT: KITTITAS COUNTY, UPPER DISTRICT COURT REMODEL

THIS PROPOSAL IS TO PROVIDE LABOR AND MATERIAL FOR THE FOLLOWING:

REVISE OVERHEAD DOOR 124c TO INCREASE ITS HEIGHT FROM 9' TO ROUGHLY 10' (MATCHING THE HEIGHT OF THE EXISTING OVERHEAD DOOR).

1. RETAIN THE DOORS CURRENT PANELS AND ADD (1) ADDITIONAL 15" TOP PANEL CUT TO SIZE AS NEEDED WITH ALUMINUM REINFORCING TOP-TRIM. THE TOP PANEL SHALL BE OF SIMILAR CONSTRUCTION TO REMAINDER OF THE DOOR (INSULATED WITH STUCCO-EMBOSSED SKINS), BUT BOTH INTERIOR AND EXTERIOR SKINS SHALL BE 27 GA. STEEL.
2. REMOVE AND REINSTALL DOOR TRACKS, TROLLEY OPERATOR, SENSORS, AND OTHER ASSOCIATED HARDWARE AS REQUIRED. PROVIDING AND INSTALLING EXTENSIONS TO THE DOOR TRACKS.

TOTAL COST OF THIS PROPOSAL.....\$ 980.00

PLEASE ALLOW 2 WEEK LEAD TIME.

PLEASE CALL IF YOU HAVE ANY QUESTIONS.

ALL ELECTRICAL WORK BY OTHERS, NO ELECTRICAL WORK IS INCLUDED IN THIS PROPOSAL

ALL MATERIAL IS TO BE AS SPECIFIED ABOVE. ALL WORK TO BE COMPLETED IN A WORKMANLIKE MANNER ACCORDING TO STANDARD PRACTICES. ANY ALTERATION OR DEVIATION FROM ABOVE SPECIFICATIONS INVOLVING EXTRA COST WILL BE EXECUTED ONLY UPON WRITTEN ORDERS, AND BECOME AN EXTRA CHARGE ABOVE THIS PROPOSAL. ALL AGREEMENTS CONTINGENT UPON STRIKES, ACCIDENTS OR DELAYS BEYOND OUR CONTROL. OWNER TO CARRY FIRE AND OTHER NECESSARY INSURANCE. OUR WORKERS ARE FULLY COVERED BY WORKMEN COMPENSATION INSURANCE.

CONDITIONS OF THIS PROPOSAL:

1. THE ABOVE PROPOSAL IS SUBJECT TO WITHDRAWAL OR REVISION IF NOT ACCEPTED WITHIN 30 DAYS.
2. IF INSTALLATION IS REQUIRED TO BE PERFORMED OTHER THAN NORMAL BUSINESS HOURS (MONDAY THROUGH FRIDAY 6:00 AM TO 5:00 PM). IT IS UNDERSTOOD THAT OVERTIME LABOR RATE WILL BE ASSESSED. TIME LOSS, EXTRA TRIPS, LOAD AND UNLOADING TIME CAUSED BY CUSTOMER NOT BEING READY AT TIME OF SCHEDULED INSTALLATION AND NOT NOTIFYING S.C.I. DOOR 24 HOURS IN ADVANCE WILL BE CHARGED AT NORMAL SERVICE RATE PER MAN HOUR OF TIME LOST.
3. WHEN REQUIRED, SHOP DRAWINGS WILL BE FURNISHED. WHEN APPROVED BY THE PURCHASER, CONTRACTOR, ARCHITECT OR AGENTS REPRESENTING THEM, THEY SHALL BE DEEMED TO BE THE CORRECT INTERPRETATION OF DESIGN, PRODUCT, DIMENSIONS, AND QUANTITY. CUSTOMER AGREES TO PAY ANY AND ALL RESTOCK CHARGES AND TRANSPORTATION COSTS CAUSED BY CHANGES MADE AFTER ACCEPTANCE OF SHOP DRAWINGS AND OR THIS PROPOSAL.
4. THE CUSTOMER AGREES TO RECEIVE, UNLOAD AND PROVIDE ADEQUATE STORAGE FACILITY FOR MATERIALS DELIVERED. FURNISH NECESSARY LIGHT, POWER, AND FORK LIFT IF ONE IS REQUIRED FOR TYPE OF DOOR OR INSTALLATION.
5. NO BACK CHARGES WILL BE ACCEPTED BY S.C.I. DOOR UNLESS SPECIFICALLY AGREED UPON IN WRITING.
6. S.C.I. DOOR ACCEPTS NO LIABILITY FOR LOSS OR DAMAGES ARISING FROM DELAYS CAUSED BY INCORRECT OR INCOMPLETE DATA, BY TYPOGRAPHICAL ERRORS, BY CHANGES MADE BY OTHERS, OR TO OBTAIN MATERIAL OR BY DELAYS OF TRANSPORTATION CARRIERS OR BY ANY OTHER CAUSES WHATSOEVER BEYOND OUR CONTROL.
7. SALES TAX NOT INCLUDED UNLESS SHOWN AS SEPARATE COST ITEM.
8. THIS PROPOSAL SHALL NOT BE BINDING ON THIS COMPANY UNTIL SIGNED OR LATER APPROVED IN WRITING, BY AN OFFICER OF THIS COMPANY.
9. SHOULD THE PURCHASER TENDER HIS OWN PURCHASE ORDER OR CONTRACT BY USE OR INFORMATION AND OR PRICES LISTED IN THIS PROPOSAL, CONDITIONS OF THIS PROPOSAL SHALL BE A PART OF THAT AGREEMENT WHETHER OR NOT THIS PROPOSAL IS ACKNOWLEDGED IN THAT CONTRACT OR PURCHASE ORDER.

AUTHORIZED SIGNATURE

Chris Klingele

S.C.I. DOOR

CONT. # SCIDO**022MO

* ALL PRICES ARE SUBJECT TO SALES TAX UNLESS OTHERWISE NOTED

* ALL INVOICES ARE DUE UPON RECEIPT UNLESS PRIOR ARRANGEMENTS ARE MADE:

* PROPOSAL GOOD FOR 30 DAYS

ACCEPTANCE: THE ABOVE PRICES, SPECIFICATIONS AND CONDITIONS ARE SATISFACTORY AND ARE HEREBY ACCEPTED. YOU ARE AUTHORIZED TO DO THE WORK AS SPECIFIED. IF INCURRED, COLLECTION COSTS, INCLUDING REASONABLE ATTORNEY'S FEES, MAY BE ADDED TO YOUR ACCOUNT BALANCE. DELINQUENT ACCOUNTS MAY BE CLOSED TO FURTHER CREDIT.

PLEASE INITIAL ALL PROPOSAL PACKAGES ACCEPTED AND SIGN BELOW:



ARCHITECTS
RASMUSSEN
TRIEBELHORN

Number 9 Saint Helens, Ste. D
The Henry Drum House
Tacoma WA 98402

Phone: 253 572-5511
Fax: 253 572-5515
www.a-r-t.org

Peter T.S. Rasmussen, FAIA, Principal
Kern D. Triebelhorn, AIA, Principal
Rhonda A. Gillogly, AIA, Principal

PROPOSAL REQUEST

- ☒ Owner
☒ Architect
☒ Contractor
☐ Field
☐

AIA DOCUMENT G709

PROJECT:

Kittitas County
Upper District Court Remodel
700 East 1st Street
Cle Elum, WA 98922

PROPOSAL REQUEST NO: **28**

REFERENCE NO.

OWNER:

Kittitas County
205 West 5th Avenue
Ellensburg, WA 98926

ISSUE DATE: **June 20, 2013**

OWNER'S PROJECT NO. **2012-004**

TO:

M. Sevigny Construction, Inc.
1251 Lucy Lane
Zillah, WA 98953

ART'S PROJECT NO. **1204**

CONTRACT DATED: **January 8, 2013**

Please submit an itemized quotation for changes in the Contract Sum and/or Time incidental to proposed modifications to the Contract Documents described herein.

THIS IS NOT A CHANGE ORDER NOR A DIRECTION TO PROCEED WITH THE WORK DESCRIBED HEREIN.

Description: (Written description of the Work)

Revise overhead door 124c to increase its height from 9' to roughly 10' (matching the height of the existing overhead door).

1. Retain the door's current panels and add (1) additional 15" top panel cut to size as needed with aluminum reinforcing top-trim. The top panel shall be of similar construction to remainder of the door (insulated with stucco-embossed skins), but both interior and exterior skins shall be 27 GA. aluminum.
2. Revise, reframe and refinish surrounding opening, reusing header and other materials as much as economically possible to accommodate the revised door.
3. Remove and reinstall door tracks, trolley operator, sensors, and other associated hardware as required. Providing and installing extensions to the door tracks.

Attachments: (List attached documents that support description)

None

ARCHITECTS RASMUSSEN TRIEBELHORN

By: David L. Head

M SEVIGNY CONSTRUCTION INC.

1212 N 16th AVENUE #1

YAKIMA, WA. 98902

Upper District Court Remodel

KITTITAS COUNTY

PROJECT # PW12-022

DATE: 7/9/2013

PROPOSAL: COP 29

Remove acoustical wall panels

#	ITEM DETAIL		SUB CONTRACTOR	GENERAL CONTRACTOR		TOTAL
1	There is a Zero gain from deleting these items as			-		-
2	any savings was used to tape, texture and paint the wall.					-
3		-			-	-
4		-				-
5					-	-
6					-	-
7					-	-
8						-
9						-
10						-
11						-
12						-
	SUBTOTAL	-	-	-	-	-
		-			-	-
	SUBTOTAL	-	-	-	-	-
	SUBCONTRACTOR 8%		-		-	-
	GENERAL 15%	-		-	-	-
	SUBTOTAL	-	-	-	-	-
	BOND AND INSURANCE 2.5%	-	-	-	-	-
	SAFETY 2%	-	-	-	-	-
	TOTAL PROPOSAL	-	-	-	-	-
	TIME REQUIRED TBD DAYS					
	M SEVIGNY CONSTRUCTION INC.					
	MATTHEW SEVIGNY					

APPROVED FOR CHANGE ORDER #3
David Head, ART 9/6/2013



ARCHITECTS
RASMUSSEN
TRIEBELHORN

Number 9 Saint Helens, Ste. D
The Henry Drum House
Tacoma WA 98402

Phone: 253 572-6511
Fax: 253 572-6515
www.a-r-t.org

Peter T.S. Rasmussen, FAIA, Principal
Karin D. Triebelhorn, AIA, Principal
Rhonda A. Grogg, AIA, Principal

PROPOSAL REQUEST

- ☒ Owner
☒ Architect
☒ Contractor
☐ Field
☐

AIA DOCUMENT G709

PROJECT:
**Kittitas County
Upper District Court Remodel
700 East 1st Street
Cle Elum, WA 98922**

PROPOSAL REQUEST NO: **29**

REFERENCE NO.

OWNER:
**Kittitas County
205 West 5th Avenue
Ellensburg, WA 98926**

ISSUE DATE: **June 25, 2013**

OWNER'S PROJECT NO. **2012-004**

TO:
**M. Sevigny Construction, Inc.
1251 Lucy Lane
Zillah, WA 98953**

ART'S PROJECT NO. **1204**

CONTRACT DATED: **January 8, 2013**

Please submit an itemized quotation for changes in the Contract Sum and/or Time incidental to proposed modifications to the Contract Documents described herein.

THIS IS NOT A CHANGE ORDER NOR A DIRECTION TO PROCEED WITH THE WORK DESCRIBED HEREIN.

Description: (Written description of the Work)

1. Delete acoustic glu-on tile from the south, east and west walls of Courtroom 111, as illustrated in the interior elevations on sheet A5.0 and details 721 and 725 on sheet A7.1.
2. Delete the "stepped" 1 1/4" x 3/4" wood trim associated with the acoustic tile noted in item 1 from the east and west walls of Courtroom 111.

Attachments: (List attached documents that support description)
None

ARCHITECTS RASMUSSEN TRIEBELHORN

By: David L. Head

M SEVIGNY CONSTRUCTION INC.**1212 N 16th AVENUE #1****YAKIMA, WA. 98902****Upper District Court Remodel****KITTITAS COUNTY****PROJECT # PW12-022****DATE: 7/9/2013****PROPOSAL: COP 30****Loose VCT removal and prep**

#	ITEM DETAIL		SUB CONTRACTOR	GENERAL CONTRACTOR	TOTAL
1	M Sevigny			320.00	320.00
2					-
3		-		-	-
4		-			-
5				-	-
6				-	-
7				-	-
8					-
9					-
10					-
11					-
12					-
	SUBTOTAL	-	-	320.00	320.00
		-		-	-
	SUBTOTAL	-	-	320.00	320.00
	SUBCONTRACTOR 8%		-		-
	GENERAL 15%	-		48.00	48.00
	SUBTOTAL	-	-	368.00	368.00
	BOND AND INSURANCE 2.5%	-	-	9.20	9.20
	SAFETY 2%	-	-	7.36	7.36
	TOTAL PROPOSAL	-	-	384.56	384.56
	TIME REQUIRED 0 15 DAYS				
	M SEVIGNY CONSTRUCTION INC.				
	MATTHEW SEVIGNY				

(D.L.H. 9/10/2013)

APPROVED FOR CHANGE ORDER #3
David Head, ART 9/6/2013



ARCHITECTS
RASMUSSEN
TRIEBELHORN

Number 9 Saint Helens, Ste. D
The Henry Drum House
Tacoma, WA 98402

Phone: 253 572-5511
Fax: 253 572-5515
www.a-r-t.org

Peter T.S. Rasmussen, FAIA, Principal
Kenn D. Triebelhorn, AIA, Principal
Rhonda A. Gillogly, AIA, Principal

PROPOSAL REQUEST

- ☒ Owner
☒ Architect
☒ Contractor
☐ Field
☐

AIA DOCUMENT G709

PROJECT:
Kittitas County
Upper District Court Remodel
700 East 1st Street
Cle Elum, WA 98922

PROPOSAL REQUEST NO: **30**

REFERENCE NO.

OWNER:
Kittitas County
205 West 5th Avenue
Ellensburg, WA 98926

ISSUE DATE: **June 28, 2013**

OWNER'S PROJECT NO. **2012-004**

TO:
M. Seigny Construction, Inc.
1251 Lucy Lane
Zillah, WA 98953

ART'S PROJECT NO. **1204**

CONTRACT DATED: **January 8, 2013**

Please submit an itemized quotation for changes in the Contract Sum and/or Time incidental to proposed modifications to the Contract Documents described herein.

THIS IS NOT A CHANGE ORDER NOR A DIRECTION TO PROCEED WITH THE WORK DESCRIBED HEREIN.

Description: (Written description of the Work)

At areas of carpet to be installed over existing VCT, remove any loose tiles and provide leveling compound/ thinset as required for a smooth solid surface ready to receive new carpet. Costs associated with this PR shall exclude any previously submitted for work related to COP 23 (CCP 7) & CO 2.

Attachments: (List attached documents that support description)
None

ARCHITECTS RASMUSSEN TRIEBELHORN

By: David L. Head

M SEVIGNY CONSTRUCTION INC.
1212 N 16th AVENUE #1
YAKIMA, WA. 98902

Upper Distrrict Court Remodel
 KITTITAS COUNTY
 PROJECT # PW12-022
 DATE: 7/9/2013
 PROPOSAL: COP 31
 Preventative Roof Maintenance

#	ITEM DETAIL		SUB CONTRACTOR	GENERAL CONTRACTOR		TOTAL
1	M Sevigny			1,760.00		1,760.00
2						-
3		-			-	-
4		-				-
5					-	-
6					-	-
7					-	-
8						-
9						-
10						-
11						-
12						-
	SUBTOTAL	-	-	1,760.00	-	1,760.00
		-			-	-
	SUBTOTAL	-	-	1,760.00	-	1,760.00
	SUBCONTRACTOR 8%		-			-
	GENERAL 15%	-		264.00	-	264.00
	SUBTOTAL	-	-	2,024.00	-	2,024.00
	BOND AND INSURANCE 2.5%	-	-	50.60	-	50.60
	SAFETY 2%	-	-	40.48	-	40.48
	TOTAL PROPOSAL	-	-	2,115.08	-	2,115.08
	TIME REQUIRED (D.L.H. 9/10/2013) 0 15 DAYS					
	M SEVIGNY CONSTRUCTION INC.					
	MATTHEW SEVIGNY					

APPROVED FOR CHANGE ORDER #3
 David Head, ART 9/6/2013



ARCHITECTS
RASMUSSEN
TRIEBELHORN AIA/PS

Number 9 Saint Helens, Ste. D
The Henry Drum House
Tacoma WA 98402

Phone: 253-572-5611
Fax: 253-572-5615
www.a-r-t.org

Peter T.S. Rasmussen, FAIA, Principal
Kern D. Triebelhorn, AIA, Principal
Rhonda A. Gillogly, AIA, Principal

PROPOSAL REQUEST

- ☒ Owner
☒ Architect
☒ Contractor
☐ Field
☐

AIA DOCUMENT G709

PROJECT:
**Kittitas County
Upper District Court Remodel
700 East 1st Street
Cle Elum, WA 98922**

PROPOSAL REQUEST NO: **31**

REFERENCE NO.

OWNER:
**Kittitas County
205 West 5th Avenue
Ellensburg, WA 98926**

ISSUE DATE: **June 28, 2013**

OWNER'S PROJECT NO. **2012-004**

TO:
**M. Seigny Construction, Inc.
1251 Lucy Lane
Zillah, WA 98953**

ART'S PROJECT NO. **1204**

CONTRACT DATED: **January 8, 2013**

Please submit an itemized quotation for changes in the Contract Sum and/or Time incidental to proposed modifications to the Contract Documents described herein.

THIS IS NOT A CHANGE ORDER NOR A DIRECTION TO PROCEED WITH THE WORK DESCRIBED HEREIN.

Description: (Written description of the Work)

Provide a cost for labor and materials associated with the preventative maintenance applied to the entire existing metal roof as previously requested by the owner. Work generally involves tightening of screws and application of sealant to select areas.

Attachments: (List attached documents that support description)
None

ARCHITECTS RASMUSSEN TRIEBELHORN

By: David L. Head

	M SEVIGNY CONSTRUCTION INC.					
		1212 N 16th AVENUE #1				
		YAKIMA, WA. 98902				
	Upper Distrrict Court Remodel					
	KITTITAS COUNTY					
	PROJECT # PW12-022					
	DATE: 9/8/2013					
	PROPOSAL: COP 32					
	Credit for Underslab Conduits					
#	ITEM DETAIL		SUB	GENERAL		TOTAL
			CONTRACTOR	CONTRACTOR		
1	Prater Electric		No Cost Change			-
2						-
3		-			-	-
4		-				-
5					-	-
6					-	-
7					-	-
8						-
9						-
10						-
11						-
12						-
						-
	SUBTOTAL	-	-	-	-	-
		-			-	-
	SUBTOTAL	-	-	-	-	-
	SUBCONTRACTOR 8%		-			-
	GENERAL 15%	-		-	-	-
	SUBTOTAL	-	-	-	-	-
	BOND AND INSURANCE 2.5%	-	-	-	-	-
	SAFETY 2%	-	-	-	-	-
	TOTAL PROPOSAL	-	-	-	-	-
	TIME REQUIRED TBD DAYS					
	M SEVIGNY CONSTRUCTION INC.					
	MATTHEW SEVIGNY					

APPROVED FOR CHANGE ORDER #3
David Head, ART 9/10/2013



ARCHITECTS
RASMUSSEN
TRIEBELHORN AIA/PS

Number 9 Saint Helens, Ste. D
The Henry Drum House
Tacoma WA 98402

Phone 253 572-5511
Fax 253 572-5515
www.a-rt.org

Peter T.S. Rasmussen, FAIA, Principal
Kenn D. Triebelhorn, AIA, Principal
Rhonda A. Gillogly, AIA, Principal

PROPOSAL REQUEST

- ☒ Owner
☒ Architect
☒ Contractor
☐ Field
☐

AIA DOCUMENT G709

PROJECT:
**Kittitas County
Upper District Court Remodel
700 East 1st Street
Cle Elum, WA 98922**

PROPOSAL REQUEST NO: **32**

REFERENCE NO.

OWNER:
**Kittitas County
205 West 5th Avenue
Ellensburg, WA 98926**

ISSUE DATE: **July 19, 2013**

OWNER'S PROJECT NO. **2012-004**

TO:
**M. Seigny Construction, Inc.
1251 Lucy Lane
Zillah, WA 98953**

ART'S PROJECT NO. **1204**

CONTRACT DATED: **January 8, 2013**

Please submit an itemized quotation for changes in the Contract Sum and/or Time incidental to proposed modifications to the Contract Documents described herein.

THIS IS NOT A CHANGE ORDER NOR A DIRECTION TO PROCEED WITH THE WORK DESCRIBED HEREIN.

Description: (Written description of the Work)

Refer to electrical drawings E3.0 and E5.0.

Based on site observations, it appears the following underslab conduit were not installed as called for on these drawings:

- (2) 1 1/4" conduit between each floor box and I.T. Room called for on sheet E5.0, General Note #2.
- (2) 1" conduit between each floor box and I.T. Room called for on sheet E5.0, General Note #2.
- (1) Spare 1" conduit between I.T. Room, floor boxes and court reporting desk called out on sheet E3.0, electrical note #7. Only (1) of these conduits were installed.

Due to the fact that the new court facility is nearing completion, these missing conduit will not be required to be installed. Please provide a cost credit for the conduit not installed.

Attachments: (List attached documents that support description)
None

ARCHITECTS RASMUSSEN TRIEBELHORN

By: David L. Head

	M SEVIGNY CONSTRUCTION INC.					
		1212 N 16th AVENUE #1				
		YAKIMA, WA. 98902				
	Upper Distrriect Court Remodel					
	KITTITAS COUNTY					
	PROJECT # PW12-022					
	DATE: 9/8/2013					
	PROPOSAL: COP 33					
	Additional 24 Port Patch Panel					
#	ITEM DETAIL		SUB	GENERAL		TOTAL
			CONTRACTOR	CONTRACTOR		
1	Prater Electric		357.50			357.50
2						-
3		-			-	-
4		-				-
5					-	-
6					-	-
7					-	-
8						-
9						-
10						-
11						-
12						-
						-
	SUBTOTAL	-	357.50	-	-	357.50
		-			-	-
	SUBTOTAL	-	357.50	-	-	357.50
	SUBCONTRACTOR 8%		28.60			28.60
	GENERAL 15%	-		-	-	-
	SUBTOTAL	-	386.10	-	-	386.10
	BOND AND INSURANCE 2.5%	-	9.65	-	-	9.65
	SAFETY 2%	-	7.72	-	-	7.72
	TOTAL PROPOSAL	-	403.47	-	-	403.47
	M SEVIGNY CONSTRUCTION INC.					
	MATTHEW SEVIGNY					

APPROVED FOR CHANGE ORDER #3
David Head, ART 9/10/2013



8-7-13

M. Seigny Construction
1212 N 16th Ave #1
Yakima, WA 98902

Attn. Matt Seigny

Re: Kittitas Co. Upper Court.
COP #8

The following is the cost for adding the third 24 port patch panel

Subcontract patch panel	\$250.00
Prater labor	\$75.00
P&O	\$32.50
Amount	\$357.50

Sincerely,

Tim Prater



ARCHITECTS
RASMUSSEN
TRIEBELHORN AIA/PS

Number 9 Saint Helens, Ste. D
The Henry Drum House
Tacoma WA 98402

Phone 253 572-5511
Fax 253 572-5515
www.a-rt.org

Peter T.S. Rasmussen, FAIA, Principal
Kenn D. Triebelhorn, AIA, Principal
Rhonda A. Gillogly, AIA, Principal

PROPOSAL REQUEST

- ☒ Owner
☒ Architect
☒ Contractor
☐ Field
☐

AIA DOCUMENT G709

PROJECT:

**Kittitas County
Upper District Court Remodel
700 East 1st Street
Cle Elum, WA 98922**

PROPOSAL REQUEST NO: **33**

REFERENCE NO.

OWNER:

**Kittitas County
205 West 5th Avenue
Ellensburg, WA 98926**

ISSUE DATE: **September 6, 2013**

OWNER'S PROJECT NO. **2012-004**

TO:

**M. Seigny Construction, Inc.
1251 Lucy Lane
Zillah, WA 98953**

ART'S PROJECT NO. **1204**

CONTRACT DATED: **January 8, 2013**

Please submit an itemized quotation for changes in the Contract Sum and/or Time incidental to proposed modifications to the Contract Documents described herein.

THIS IS NOT A CHANGE ORDER NOR A DIRECTION TO PROCEED WITH THE WORK DESCRIBED HEREIN.

Description: (Written description of the Work)

Provide and install in new data rack, one additional 24-port data patch panel.

Attachments: (List attached documents that support description)

None

ARCHITECTS RASMUSSEN TRIEBELHORN

By: David L. Head

	M SEVIGNY CONSTRUCTION INC.				
		1212 N 16th AVENUE #1			
		YAKIMA, WA. 98902			
	Upper Distrrict Court Remodel				
	KITTITAS COUNTY				
	PROJECT # PW12-022				
	DATE: 9/8/2013				
	PROPOSAL: COP 34				
	Misc Electrical Corrections Required by				
	Electrical Inspector				
#	ITEM DETAIL		SUB CONTRACTOR	GENERAL CONTRACTOR	TOTAL
1	Prater Electric		517.50		517.50
2					-
3		-		-	-
4		-			-
5				-	-
6				-	-
7				-	-
8					-
9					-
10					-
11					-
12					-
					-
	SUBTOTAL	-	517.50	-	517.50
		-		-	-
	SUBTOTAL	-	517.50	-	517.50
	SUBCONTRACTOR 8%		41.40		41.40
	GENERAL 15%	-		-	-
	SUBTOTAL	-	558.90	-	558.90
	BOND AND INSURANCE 2.5%	-	13.97	-	13.97
	SAFETY 2%	-	11.18	-	11.18
	TOTAL PROPOSAL	-	584.05	-	584.05
	TIME REQUIRED TBD DAYS				
	M SEVIGNY CONSTRUCTION INC.				
	MATTHEW SEVIGNY				

APPROVED FOR CHANGE ORDER #3
David Head, ART 9/10/2013



ARCHITECTS
RASMUSSEN
TRIEBELHORN AIA/PS

Number 9 Saint Helens, Ste. D
The Henry Drum House
Tacoma WA 98402

Phone 253 572-5511
Fax 253 572-5515
www.a-rt.org

Peter T.S. Rasmussen, FAIA, Principal
Kenn D. Triebelhorn, AIA, Principal
Rhonda A. Gillogly, AIA, Principal

PROPOSAL REQUEST

- ☒ Owner
☒ Architect
☒ Contractor
☐ Field
☐

AIA DOCUMENT G709

PROJECT:

**Kittitas County
Upper District Court Remodel
700 East 1st Street
Cle Elum, WA 98922**

PROPOSAL REQUEST NO: **34**

REFERENCE NO.

OWNER:

**Kittitas County
205 West 5th Avenue
Ellensburg, WA 98926**

ISSUE DATE: **September 6, 2013**

OWNER'S PROJECT NO. **2012-004**

TO:

**M. Seigny Construction, Inc.
1251 Lucy Lane
Zillah, WA 98953**

ART'S PROJECT NO. **1204**

CONTRACT DATED: **January 8, 2013**

Please submit an itemized quotation for changes in the Contract Sum and/or Time incidental to proposed modifications to the Contract Documents described herein.

THIS IS NOT A CHANGE ORDER NOR A DIRECTION TO PROCEED WITH THE WORK DESCRIBED HEREIN.

Description: (Written description of the Work)

Provide miscellaneous electrical corrections, as required by electrical inspector, determined to not be part of the original contract work.

Attachments: (List attached documents that support description)

Electrical inspector's 8/12/2013 report/correction notice excerpts.

ARCHITECTS RASMUSSEN TRIEBELHORN

By: David L. Head

2008 NEC 110 .26 -(D)	<p>Illumination shall be provided for all working spaces about service equipment, switchboards, panelboards, or motor control centers installed indoors. Additional lighting outlets shall not be required where the work space is illuminated by an adjacent light source or as permitted by 210.70(A)(1), Exception No. 1, for switched receptacles. In electrical equipment rooms, the illumination shall not be controlled by automatic means only. NEED LIGHT IN HALL AT 2 200A PANELS</p>	8/12/2013	No	
2008 NEC 314 .25 -	<p>In completed installations, each box shall have a cover, faceplate, lampholder, or luminaire canopy, except where the installation complies with 410.24(B). FURNACE DISCOS NEED COVER</p>	8/12/2013	No	
2008 NEC 406 .4 -	<p>Receptacles shall be mounted in boxes or assemblies designed for the purpose, and such boxes or assemblies shall be securely fastened in place unless otherwise permitted elsewhere in this Code. SOME RECEPS</p>	8/12/2013	No	

	LOOSE AND SET BACK TO FAR IN COURT RM. BROKEN PLATES			
--	------------------------------------------------------------	--	--	--

2008 NEC 314 .20 -	In walls or ceilings with a surface of concrete, tile, gypsum, plaster, or other noncombustible material, boxes employing a flush-type cover or faceplate shall be installed so that the front edge of the box, plaster ring, extension ring, or listed extender will not be set back of the finished surface more than 6 mm (¼ in.). In walls and ceilings constructed of wood or other combustible surface material, boxes, plaster rings, extension rings, or listed extenders shall be flush with the finished surface or project therefrom. FURNACE DISCONNECTS NEED EXTENSION	8/12/2013	No
--------------------	-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------	-----------	----
